


US 27 PROJECTS IN SOUTH LAKE COUNTY

as of 1/26/11

-Dollar amounts are calculated to the year shown
 -Dollars are in millions
 -Fiscal Year (FY) = July 1 to June 30

HIGHEST PROGRAMMED PHASE	
PHASE	COLOR
P. D. & E.	Yellow
PREL. ENG.	Blue
RIGHT OF WAY	Red
CONSTRUCTION	Green

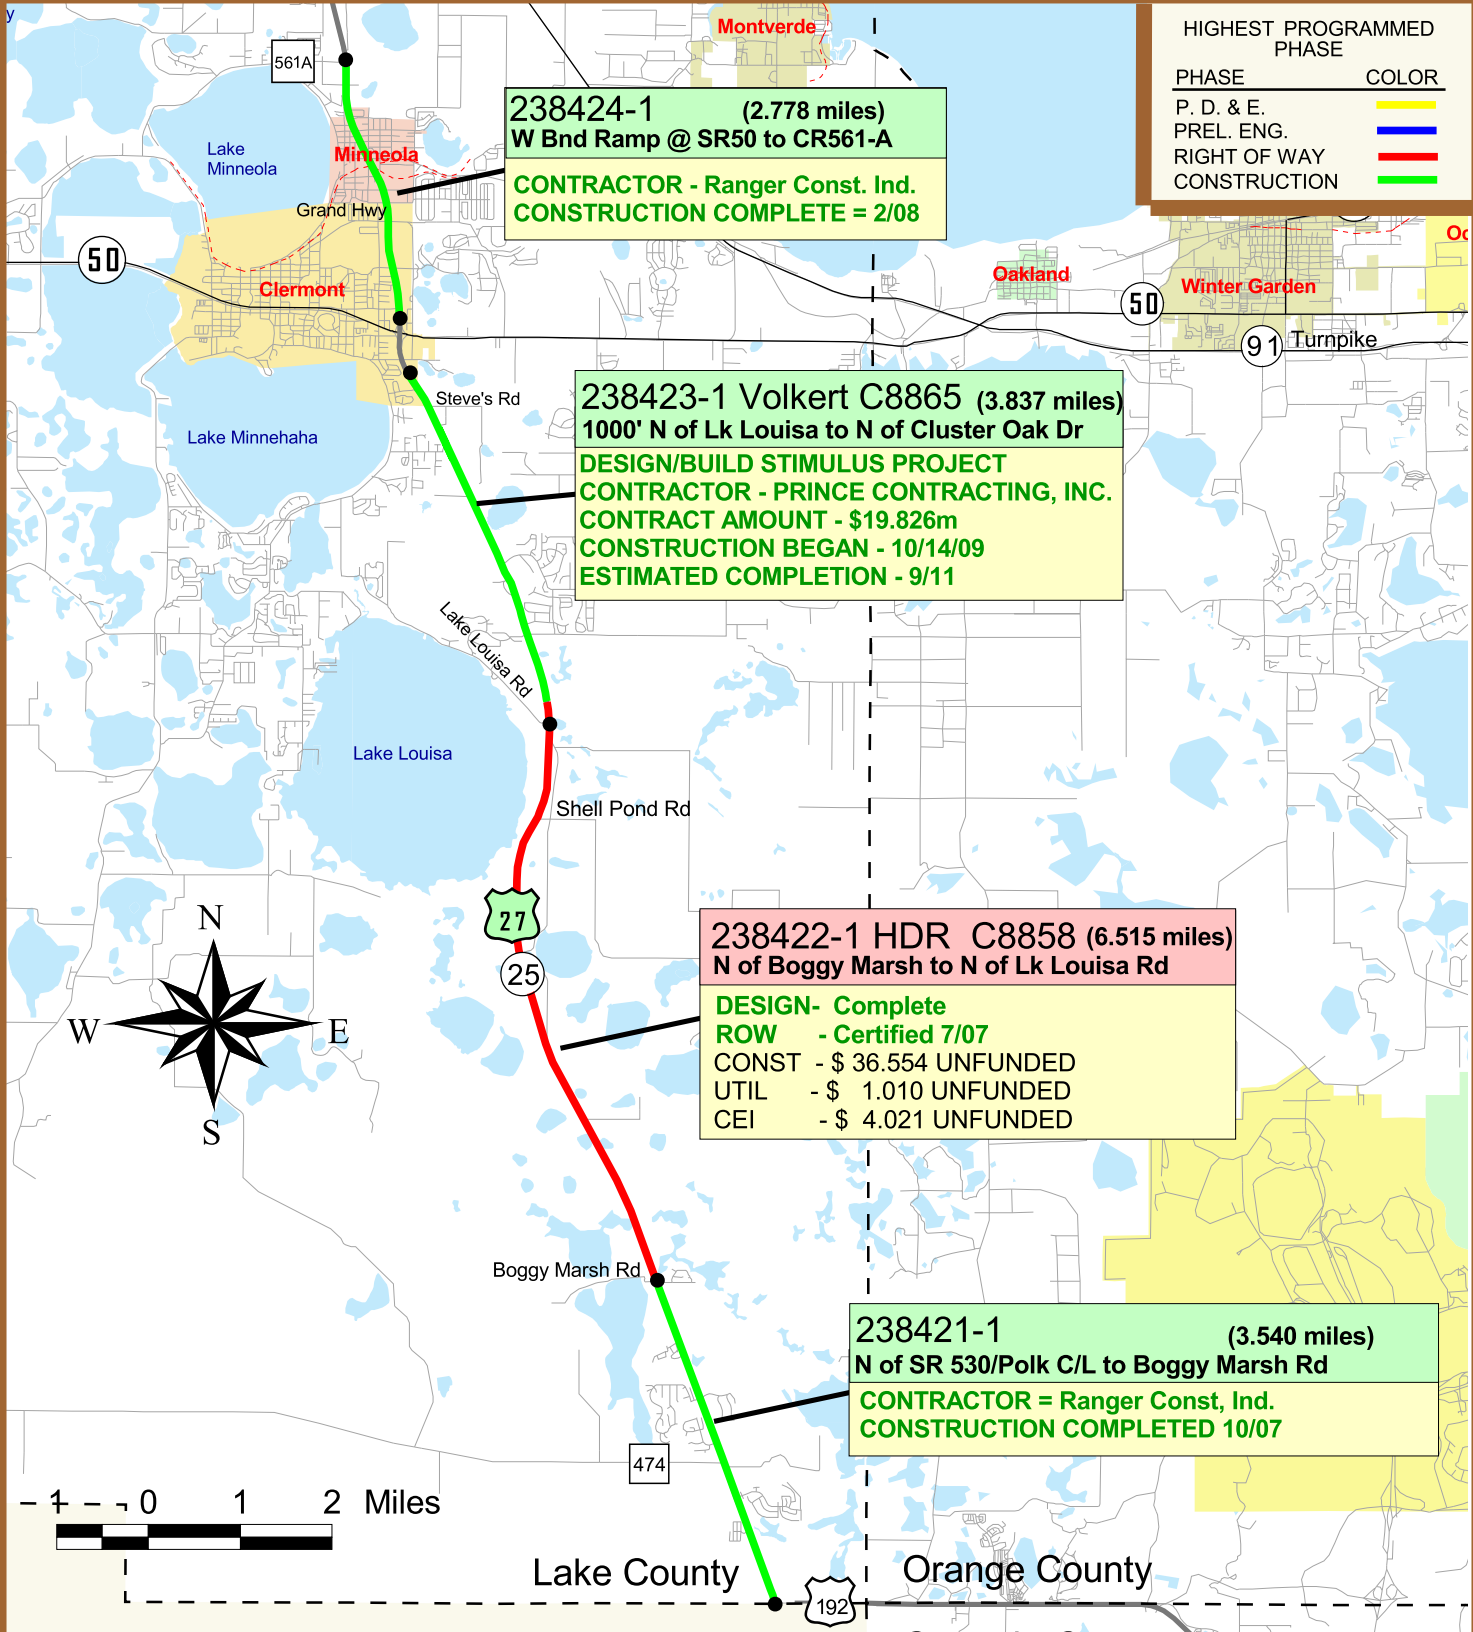

238424-1 (2.778 miles)
W Bnd Ramp @ SR50 to CR561-A
CONTRACTOR - Ranger Const. Ind.
CONSTRUCTION COMPLETE = 2/08

238423-1 Volkert C8865 (3.837 miles)
1000' N of Lk Louisa to N of Cluster Oak Dr
DESIGN/BUILD STIMULUS PROJECT
CONTRACTOR - PRINCE CONTRACTING, INC.
CONTRACT AMOUNT - \$19.826m
CONSTRUCTION BEGAN - 10/14/09
ESTIMATED COMPLETION - 9/11

238422-1 HDR C8858 (6.515 miles)
N of Bogy Marsh to N of Lk Louisa Rd
DESIGN- Complete
ROW - Certified 7/07
CONST - \$ 36.554 UNFUNDED
UTIL - \$ 1.010 UNFUNDED
CEI - \$ 4.021 UNFUNDED

238421-1 (3.540 miles)
N of SR 530/Polk C/L to Bogy Marsh Rd
CONTRACTOR = Ranger Const, Ind.
CONSTRUCTION COMPLETED 10/07

LEGEND

US Highway	
Interstate Highway	
State Highway	
County Highway	
Railroad	

