

US441 PROJECTS


As of 1/26/11

NOTE:

- Dollar amounts are calculated to the year shown.
- Dollar amounts on unfunded phases are in FY10 dollars.
- Dollars are in millions.
- Fiscal Year (FY) = July 1 to June 30

HIGHEST PROGRAMMED PHASE

PHASE	COLOR
P. D. & E.	Yellow
PREL. ENG.	Blue
RIGHT OF WAY	Red
CONSTRUCTION	Green

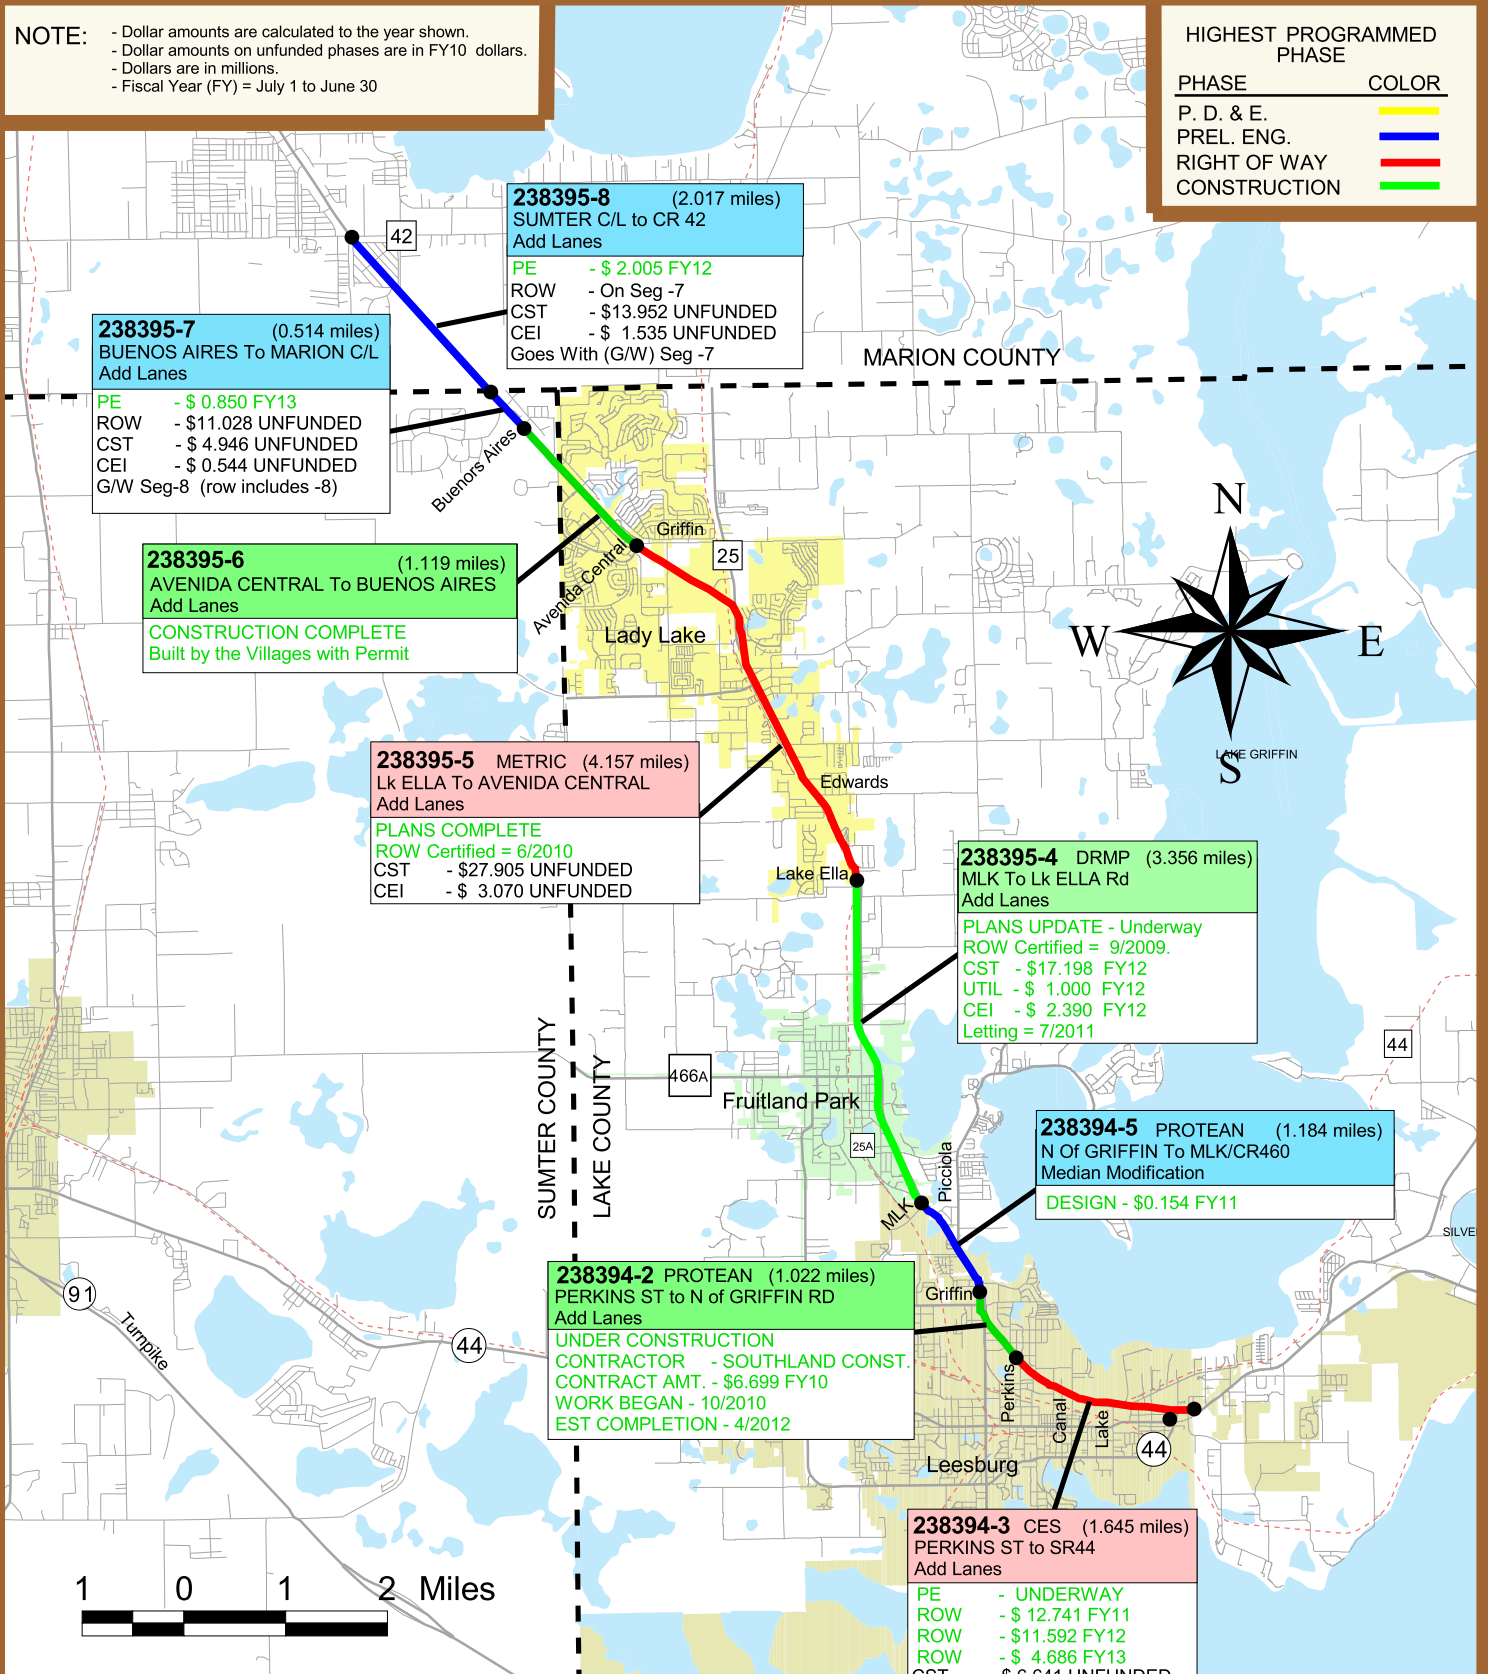

238395-7 (0.514 miles)
BUENOS AIRES To MARION C/L
 Add Lanes
 PE - \$ 0.850 FY13
 ROW - \$11.028 UNFUNDED
 CST - \$ 4.946 UNFUNDED
 CEI - \$ 0.544 UNFUNDED
 G/W Seg-8 (row includes -8)

238395-8 (2.017 miles)
SUMTER C/L to CR 42
 Add Lanes
 PE - \$ 2.005 FY12
 ROW - On Seg -7
 CST - \$13.952 UNFUNDED
 CEI - \$ 1.535 UNFUNDED
 Goes With (G/W) Seg -7

238395-6 (1.119 miles)
AVENIDA CENTRAL To BUENOS AIRES
 Add Lanes
CONSTRUCTION COMPLETE
 Built by the Villages with Permit

238395-5 METRIC (4.157 miles)
Lk ELLA To AVENIDA CENTRAL
 Add Lanes
PLANS COMPLETE
 ROW Certified = 6/2010
 CST - \$27.905 UNFUNDED
 CEI - \$ 3.070 UNFUNDED

238395-4 DRMP (3.356 miles)
MLK To Lk ELLA Rd
 Add Lanes
 PLANS UPDATE - Underway
 ROW Certified = 9/2009.
 CST - \$17.198 FY12
 UTIL - \$ 1.000 FY12
 CEI - \$ 2.390 FY12
 Letting = 7/2011

238394-5 PROTEAN (1.184 miles)
N OF GRIFFIN To MLK/CR460
 Median Modification
DESIGN - \$0.154 FY11

238394-2 PROTEAN (1.022 miles)
PERKINS ST to N of GRIFFIN RD
 Add Lanes
UNDER CONSTRUCTION
 CONTRACTOR - SOUTHLAND CONST.
 CONTRACT AMT. - \$6.699 FY10
 WORK BEGAN - 10/2010
 EST COMPLETION - 4/2012

238394-3 CES (1.645 miles)
PERKINS ST to SR44
 Add Lanes
 PE - UNDERWAY
 ROW - \$ 12.741 FY11
 ROW - \$11.592 FY12
 ROW - \$ 4.686 FY13
 CST - \$ 6.641 UNFUNDED
 CEI - \$ 0.731 UNFUNDED

LEGEND

- US Highway
- Interstate Highway
- State Highway
- County Highway
- Railroad
